


- Completed Conduit Placement
- Future Conduit Placement
- Completed Aerial Fiber Placement
- Future Aerial Placement
- Aerial strand complete pending fiber placement
- Fiber splicing complete

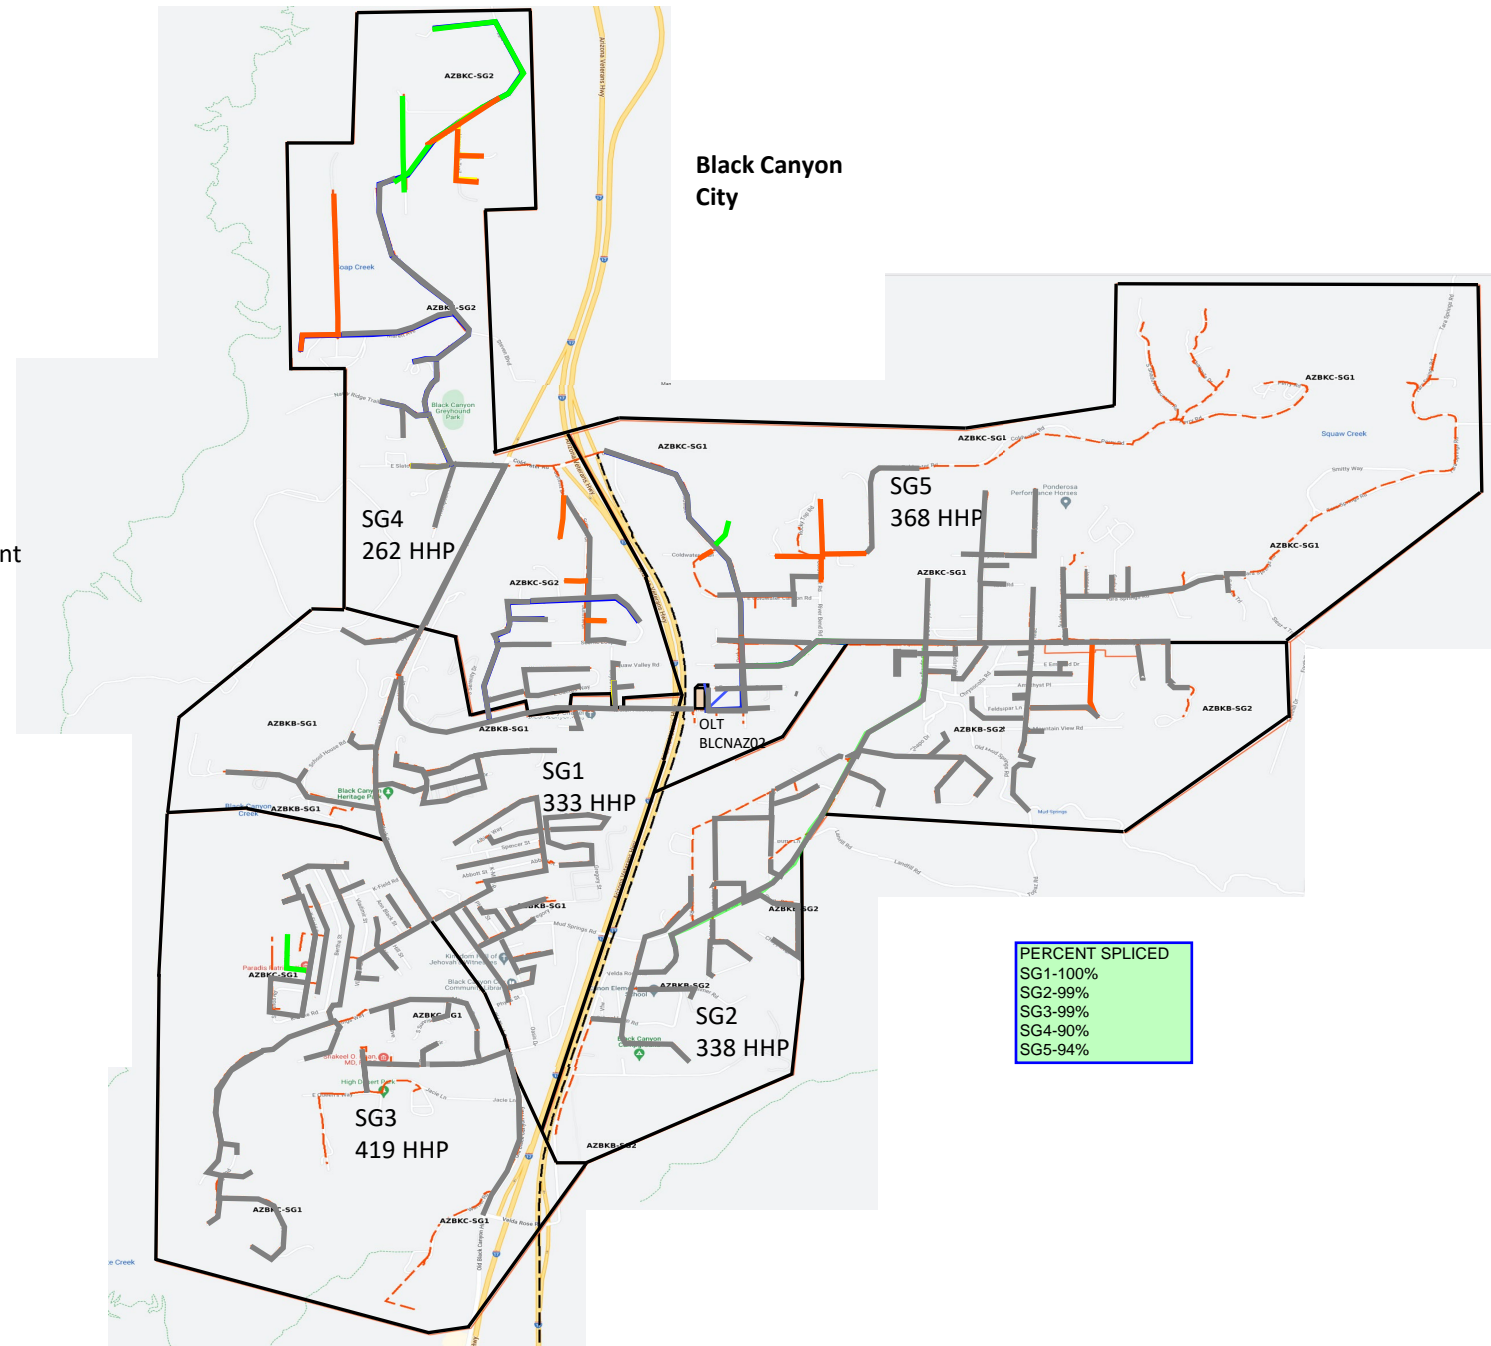

PERCENT SPLICED	
SG1-100%	
SG2-99%	
SG3-99%	
SG4-90%	
SG5-94%	
