Cox Expansion Estimated Timeline
Rev1.5

12/9/2024

Unit Service Group Project Duration (Days):	1022
Project Start:	Thu, 10/13/2022
Display Week:	1

1/25/2023

Segment - Scope	Task Owner	Days	START	END
Walk / Field Tie Point	Construction	60	10/13/2022	12/12/2022
F-DSN Complete	Design	60	11/15/2022	1/14/2023
Permits Build Task	Land Use and Compliance	548	1/14/2023	7/15/2024
Build	Construction	508	10/9/2023	2/28/2025
Splice	Construction	261	8/1/2024	4/19/2025
Testing	Construction	37	3/21/2025	4/27/2025
Release	Construction	35	3/28/2025	5/2/2025
Insert new rows ABOVE this one				

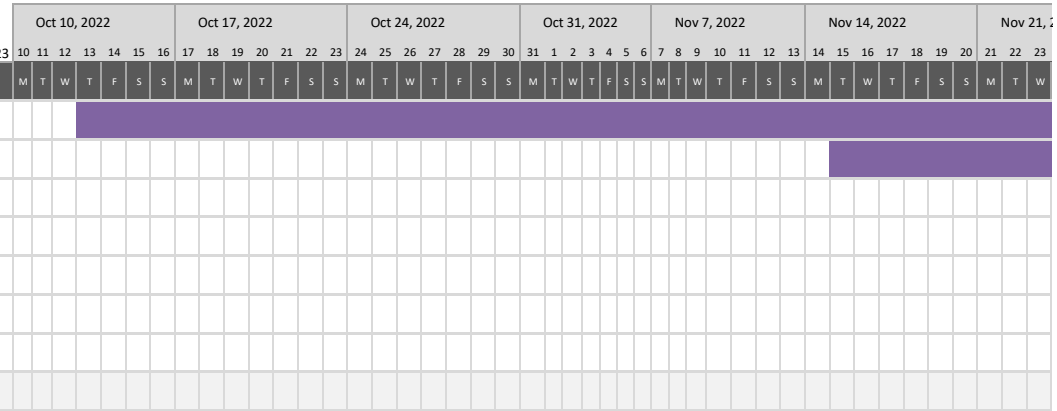

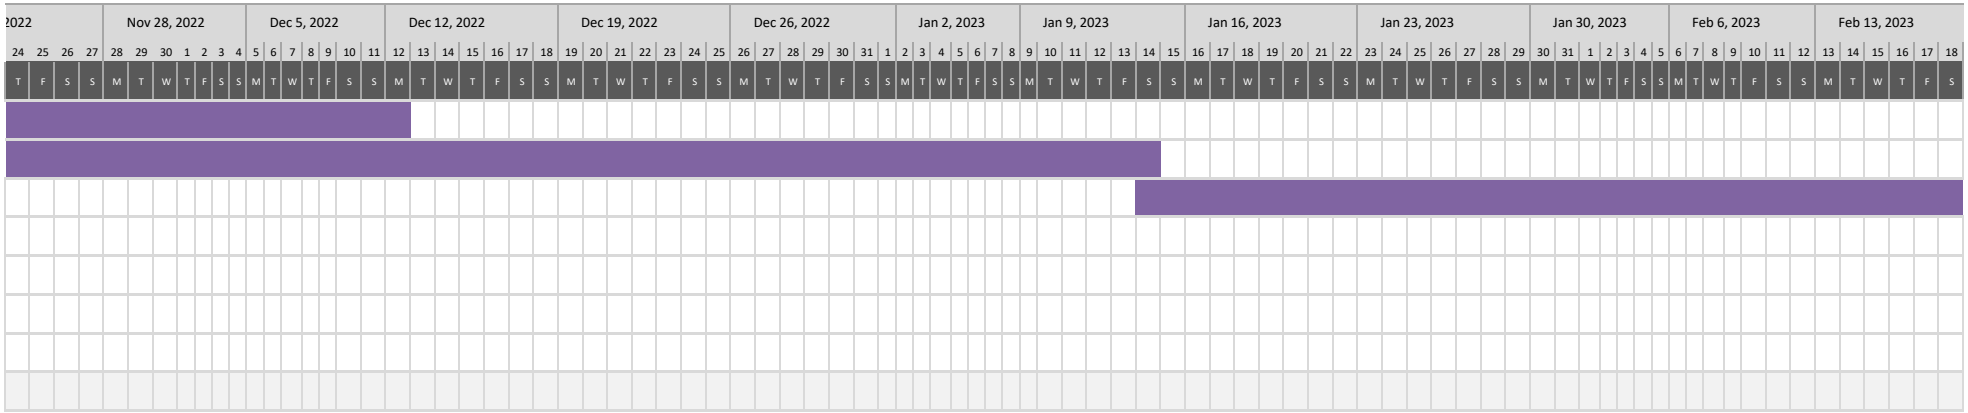
2022
Nov 28, 2022
Dec 5, 2022
Dec 12, 2022
Dec 19, 2022
Dec 26, 2022
Jan 2, 2023
Jan 9, 2023
Jan 16, 2023
Jan 23, 2023
Jan 30, 2023
Feb 6, 2023
Feb 13, 2023

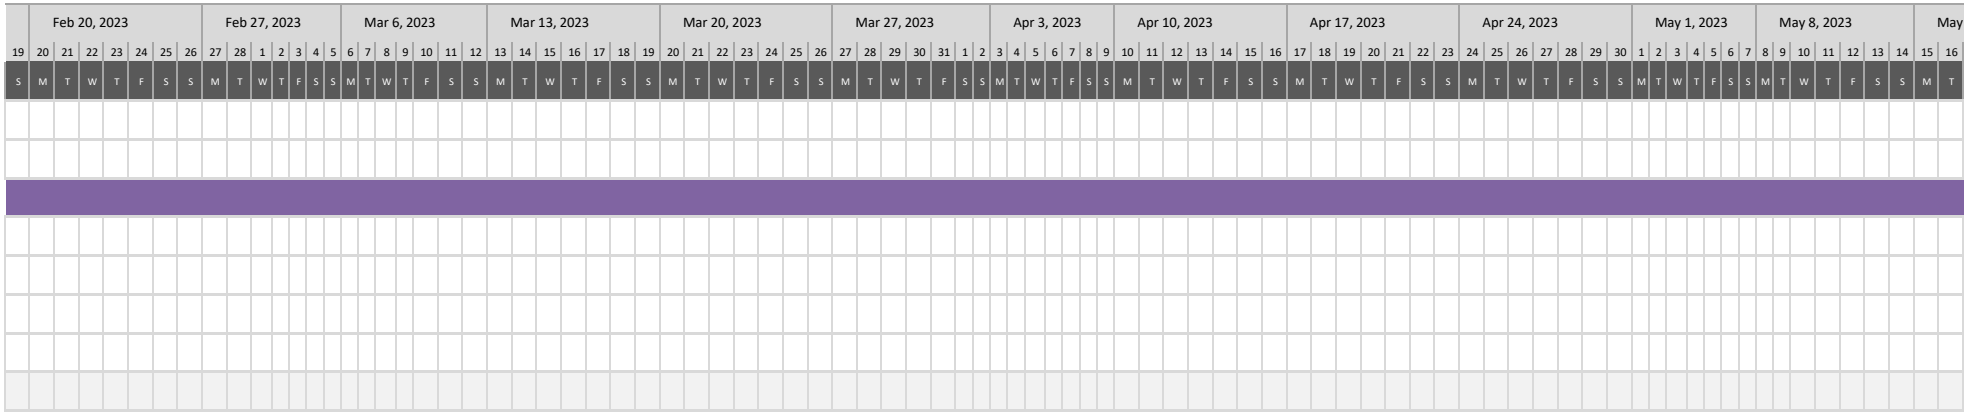
Feb 20, 2023
Feb 27, 2023
Mar 6, 2023
Mar 13, 2023
Mar 20, 2023
Mar 27, 2023
Apr 3, 2023
Apr 10, 2023
Apr 17, 2023
Apr 24, 2023
May 1, 2023
May 8, 2023
May

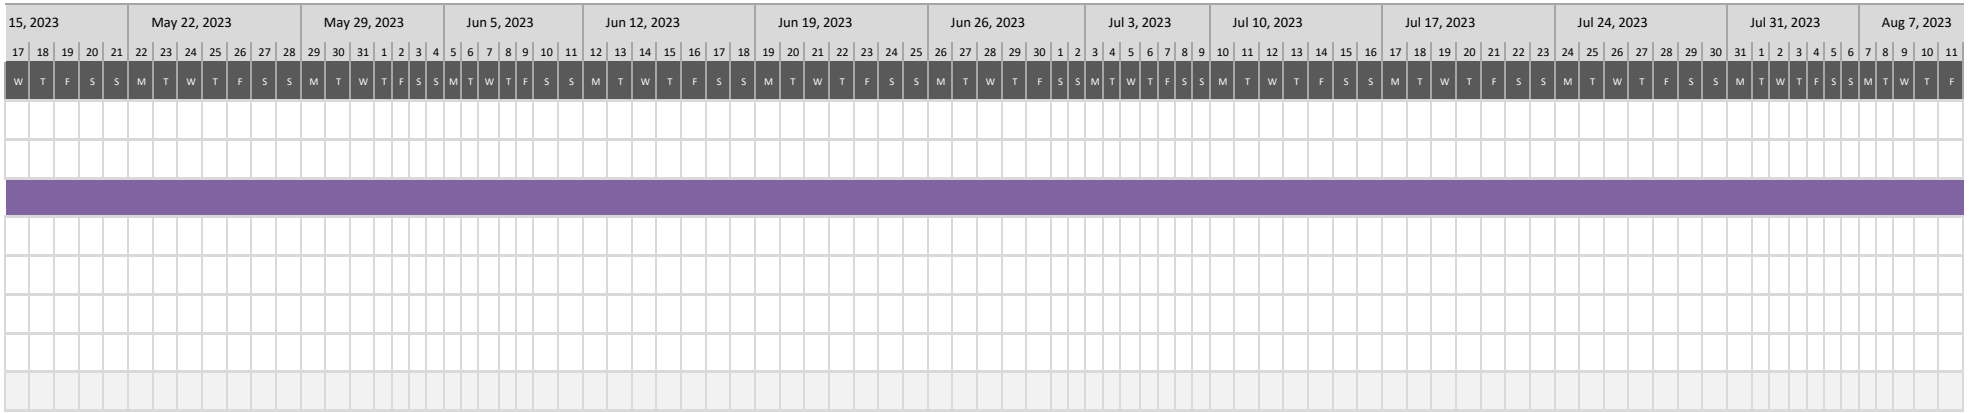
15, 2023
May 22, 2023
May 29, 2023
Jun 5, 2023
Jun 12, 2023
Jun 19, 2023
Jun 26, 2023
Jul 3, 2023
Jul 10, 2023
Jul 17, 2023
Jul 24, 2023
Jul 31, 2023
Aug 7, 2023
17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11
W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F

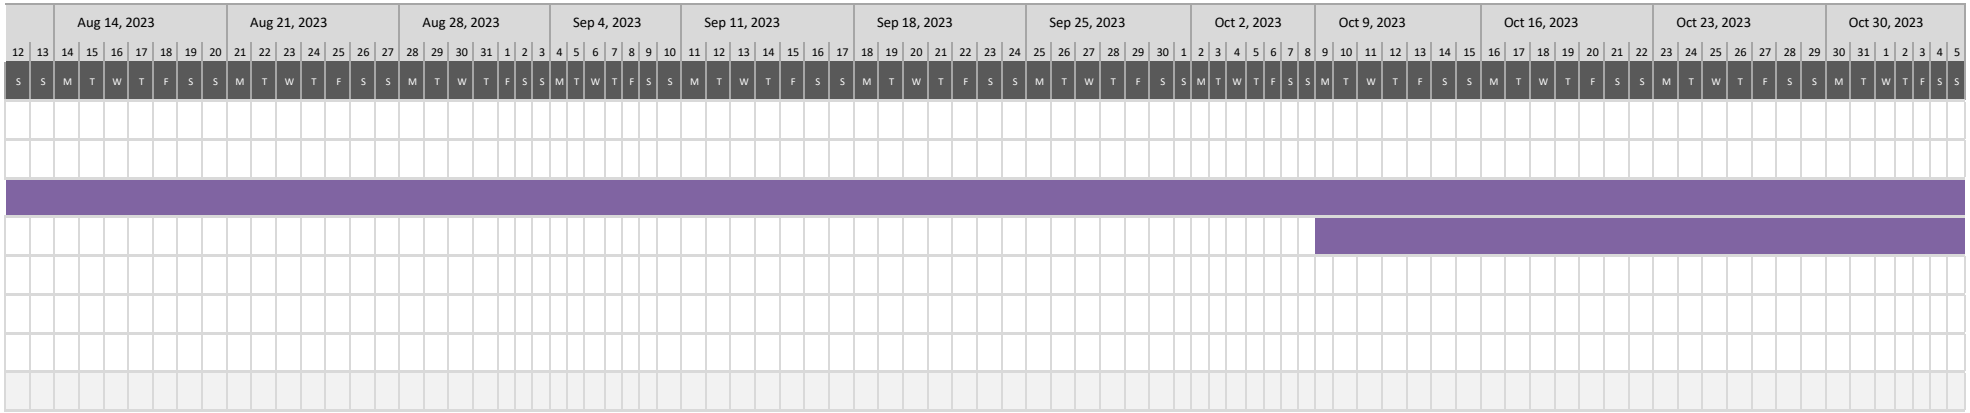
Aug 14, 2023
Aug 21, 2023
Aug 28, 2023
Sep 4, 2023
Sep 11, 2023
Sep 18, 2023
Sep 25, 2023
Oct 2, 2023
Oct 9, 2023
Oct 16, 2023
Oct 23, 2023
Oct 30, 2023

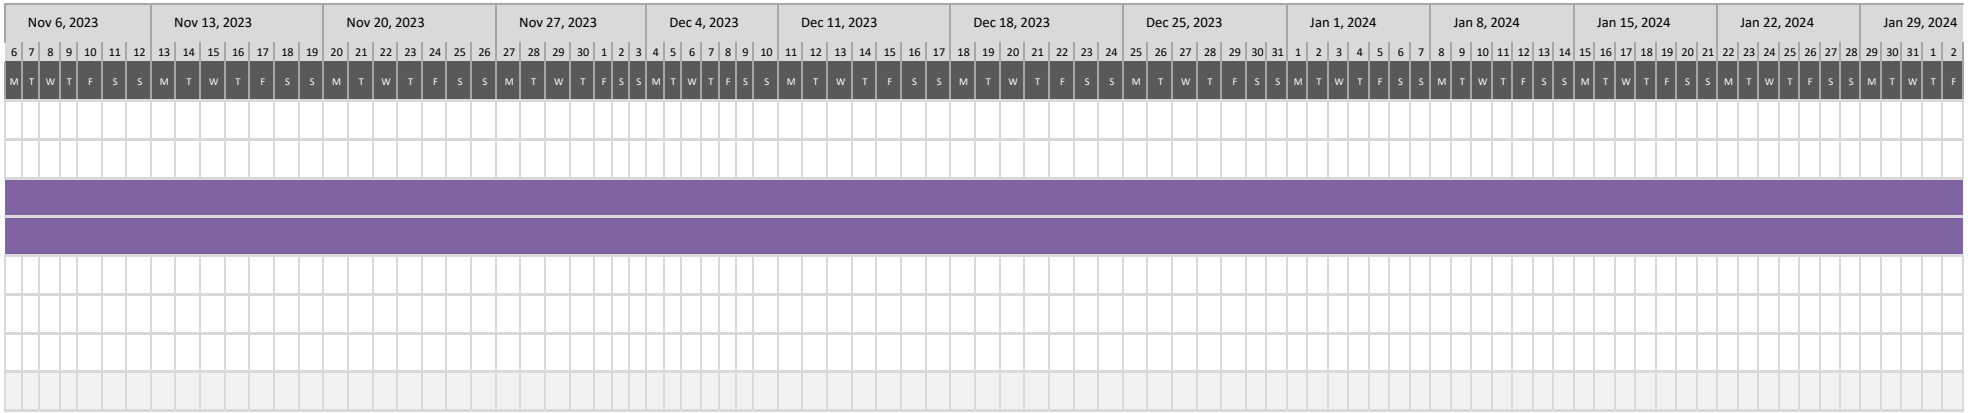
Nov 6, 2023
Nov 13, 2023
Nov 20, 2023
Nov 27, 2023
Dec 4, 2023
Dec 11, 2023
Dec 18, 2023
Dec 25, 2023
Jan 1, 2024
Jan 8, 2024
Jan 15, 2024
Jan 22, 2024
Jan 29, 2024

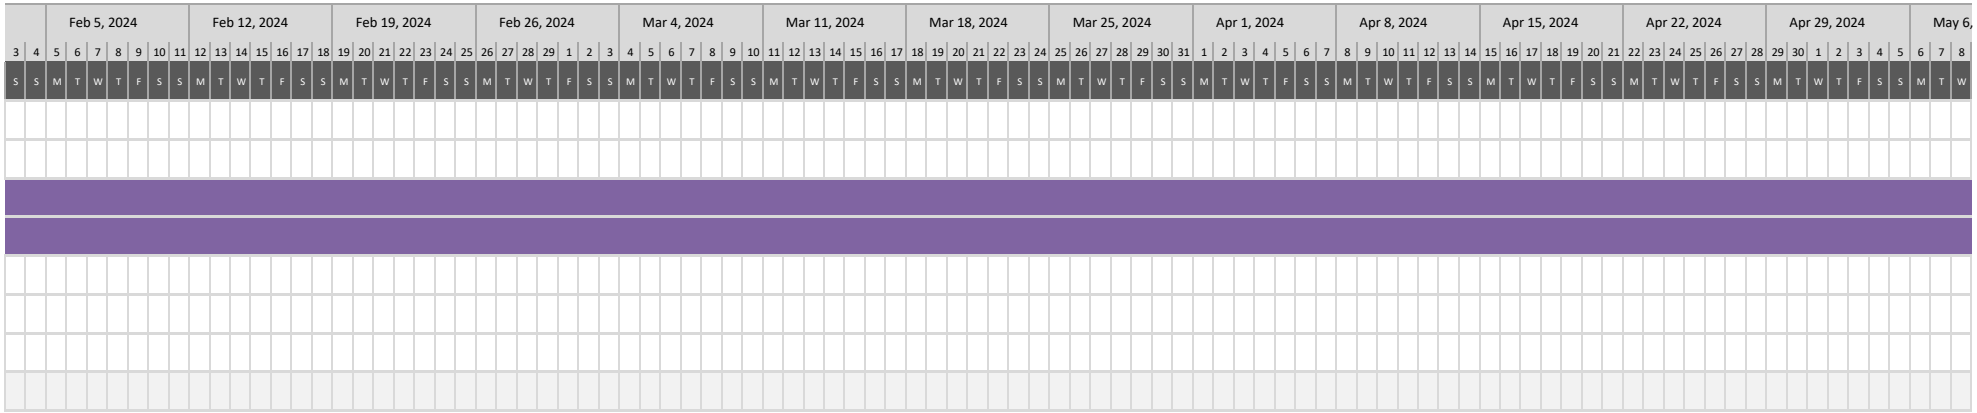
Feb 5, 2024
Feb 12, 2024
Feb 19, 2024
Feb 26, 2024
Mar 4, 2024
Mar 11, 2024
Mar 18, 2024
Mar 25, 2024
Apr 1, 2024
Apr 8, 2024
Apr 15, 2024
Apr 22, 2024
Apr 29, 2024
May 6,

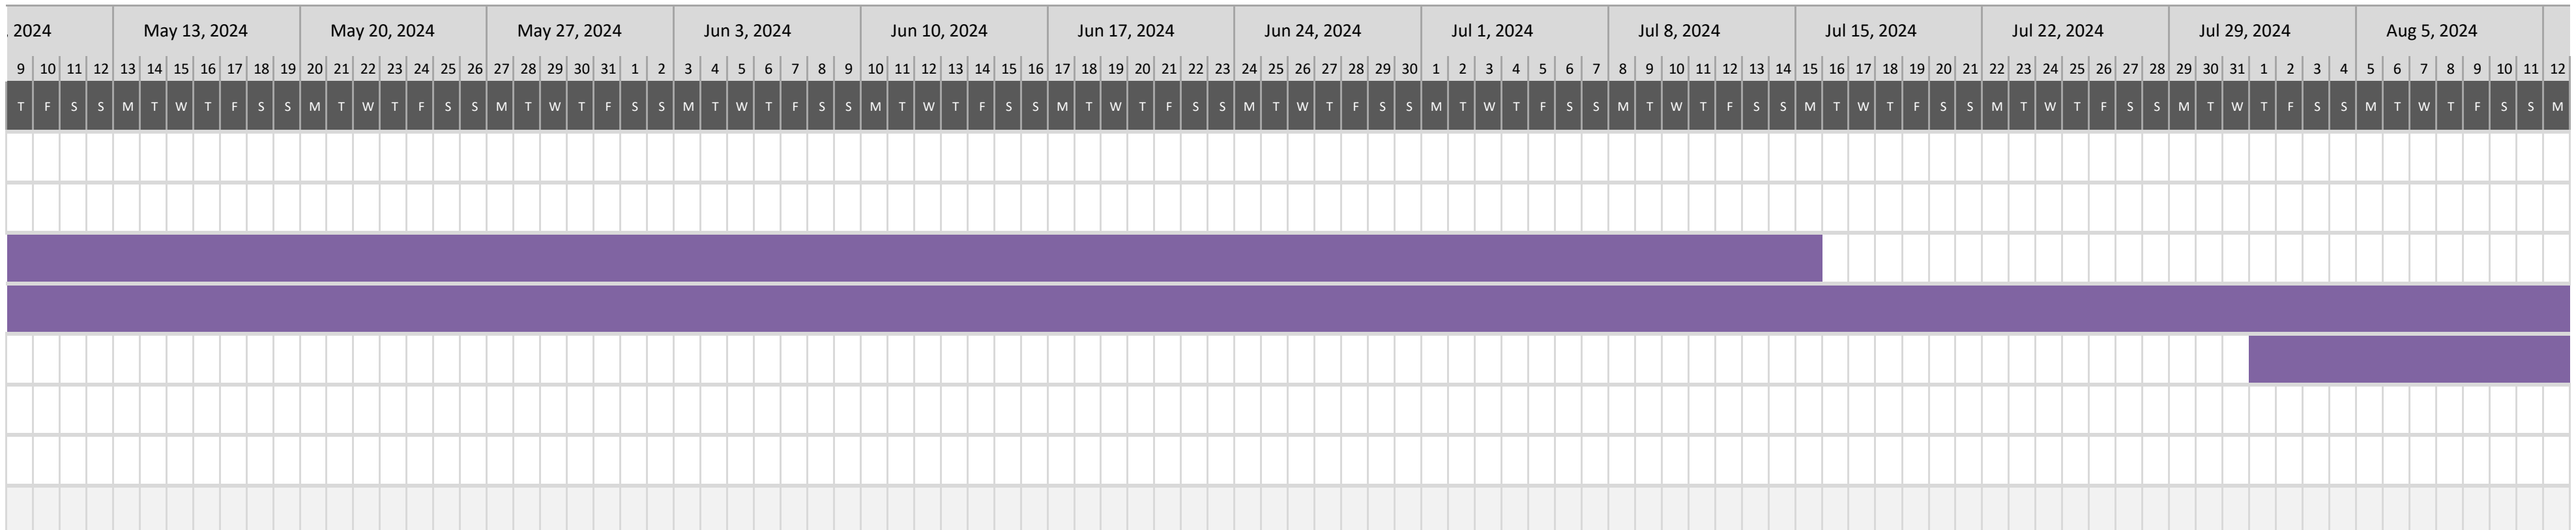
2024
May 13, 2024
May 20, 2024
May 27, 2024
Jun 3, 2024
Jun 10, 2024
Jun 17, 2024
Jun 24, 2024
Jul 1, 2024
Jul 8, 2024
Jul 15, 2024
Jul 22, 2024
Jul 29, 2024
Aug 5, 2024
9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12
T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M

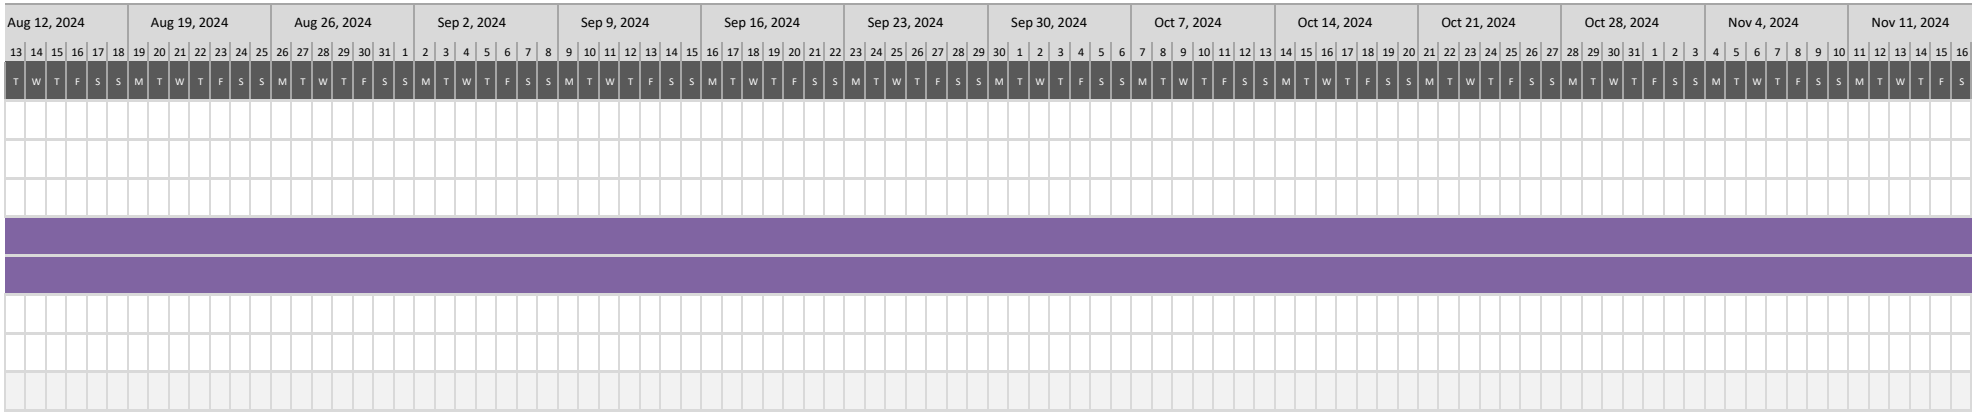
Aug 12, 2024
Aug 19, 2024
Aug 26, 2024
Sep 2, 2024
Sep 9, 2024
Sep 16, 2024
Sep 23, 2024
Sep 30, 2024
Oct 7, 2024
Oct 14, 2024
Oct 21, 2024
Oct 28, 2024
Nov 4, 2024
Nov 11, 2024
13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16
T W T F S S M T W T F S S

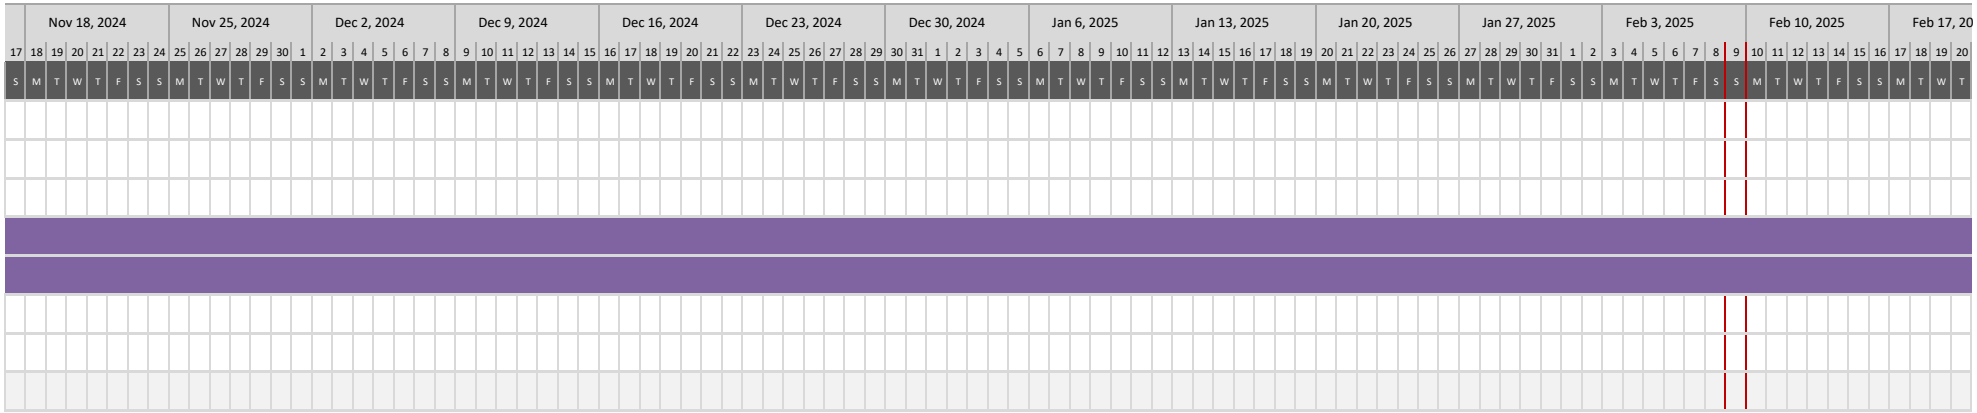
Nov 18, 2024
Nov 25, 2024
Dec 2, 2024
Dec 9, 2024
Dec 16, 2024
Dec 23, 2024
Dec 30, 2024
Jan 6, 2025
Jan 13, 2025
Jan 20, 2025
Jan 27, 2025
Feb 3, 2025
Feb 10, 2025
Feb 17, 20

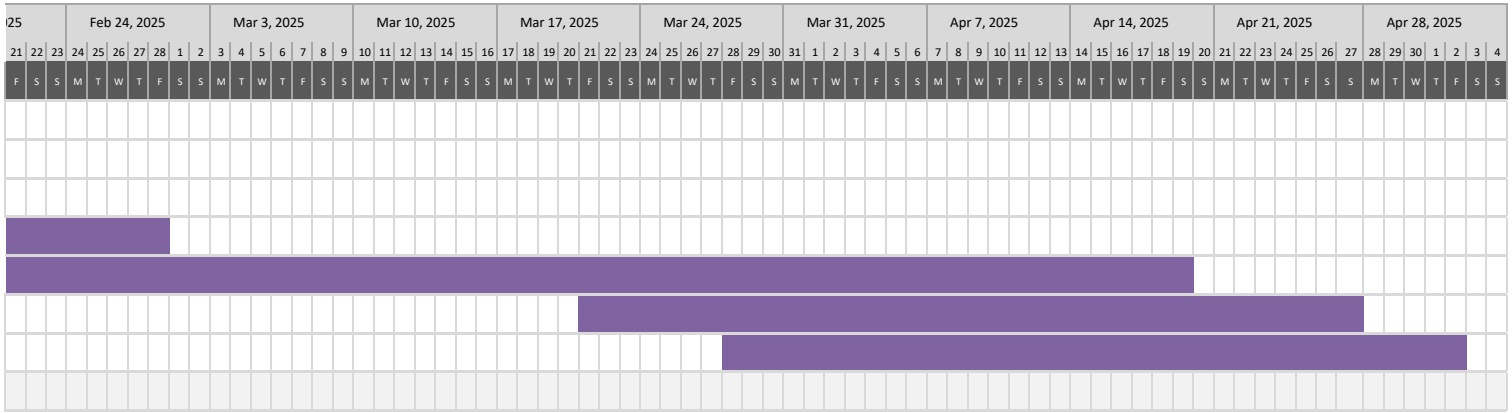
Feb 24, 2025
Mar 3, 2025
Mar 10, 2025
Mar 17, 2025
Mar 24, 2025
Mar 31, 2025
Apr 7, 2025
Apr 14, 2025
Apr 21, 2025
Apr 28, 2025
