Cox Expansion Estimated Timeline

Unit Service Group Project Duration (Days):	305
Project Start:	Thu, 10/13/2022
Display Week:	1

1/25/2023

Segment - Scope	Task Owner	Days	START	END
Walk / Field Tie Point	Construction	60	10/13/2022	12/12/2022
F-DSN Complete	Design	60	11/15/2022	1/14/2023
Permits Build Task	Land Use and Compliance	180	2/10/2023	8/9/2023
Build	Construction	210	8/10/2023	3/7/2024
Splice	Construction	120	11/20/2023	3/19/2024
Testing	Construction	45	3/20/2023	5/4/2023
Release	Construction	45	4/1/2023	5/16/2023
Insert new rows ABOVE this one				

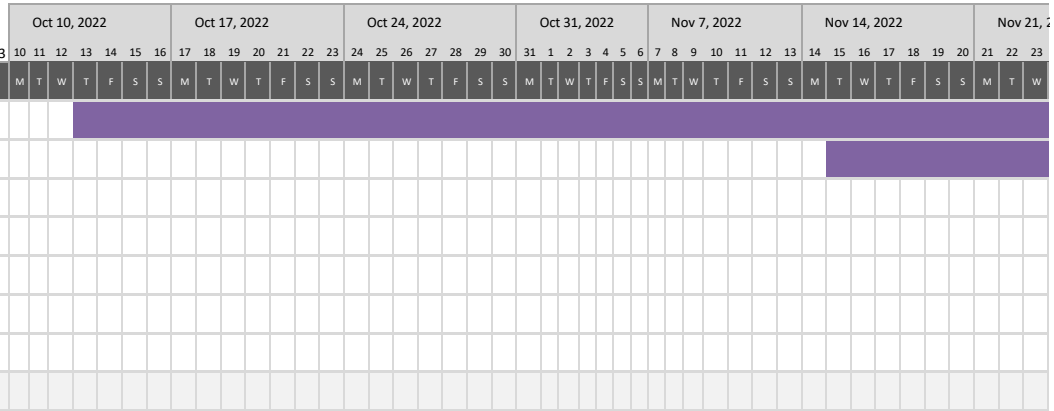

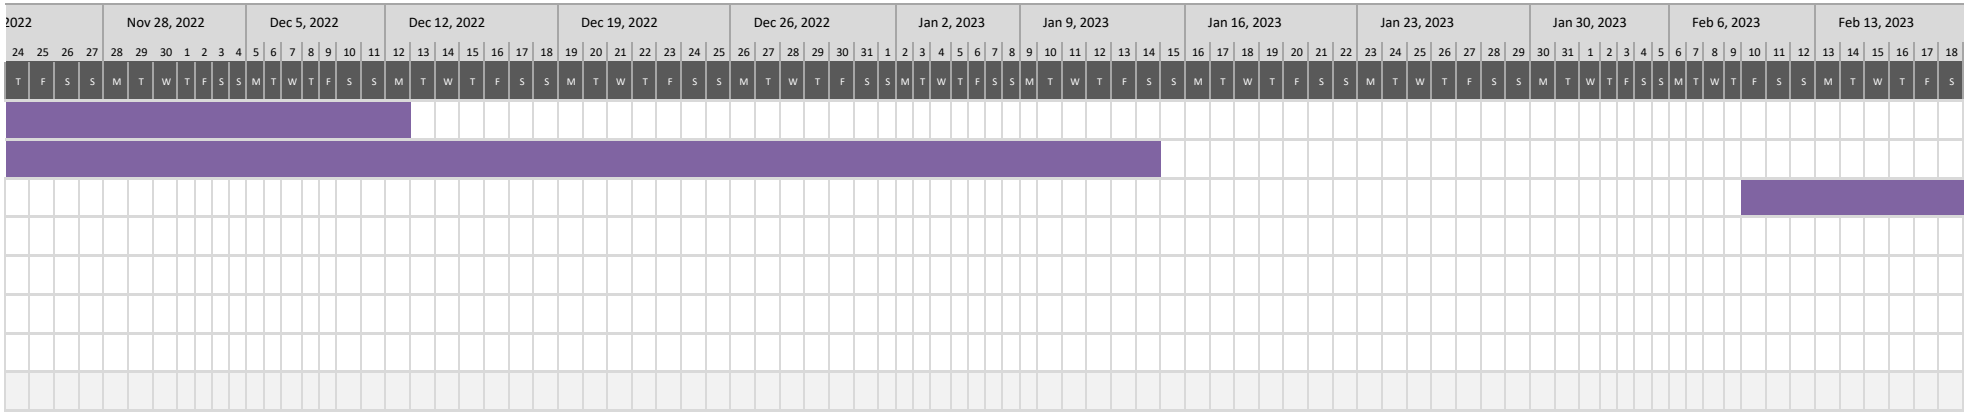
2022
Nov 28, 2022
Dec 5, 2022
Dec 12, 2022
Dec 19, 2022
Dec 26, 2022
Jan 2, 2023
Jan 9, 2023
Jan 16, 2023
Jan 23, 2023
Jan 30, 2023
Feb 6, 2023
Feb 13, 2023

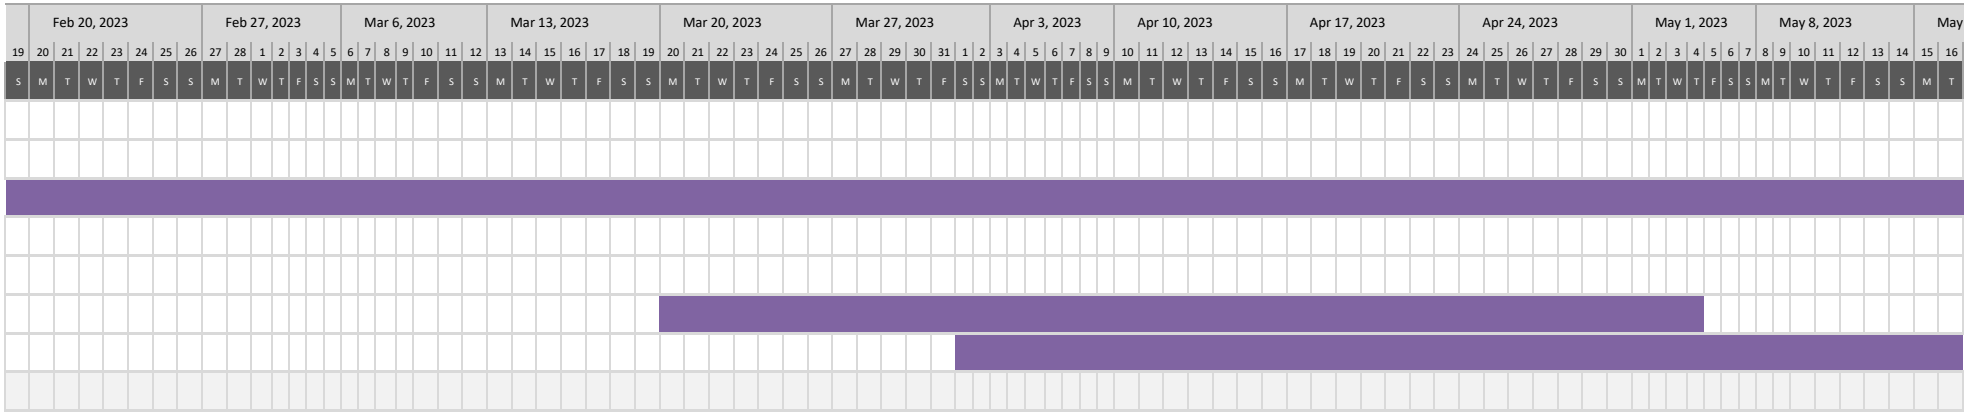
Feb 20, 2023
Feb 27, 2023
Mar 6, 2023
Mar 13, 2023
Mar 20, 2023
Mar 27, 2023
Apr 3, 2023
Apr 10, 2023
Apr 17, 2023
Apr 24, 2023
May 1, 2023
May 8, 2023
May

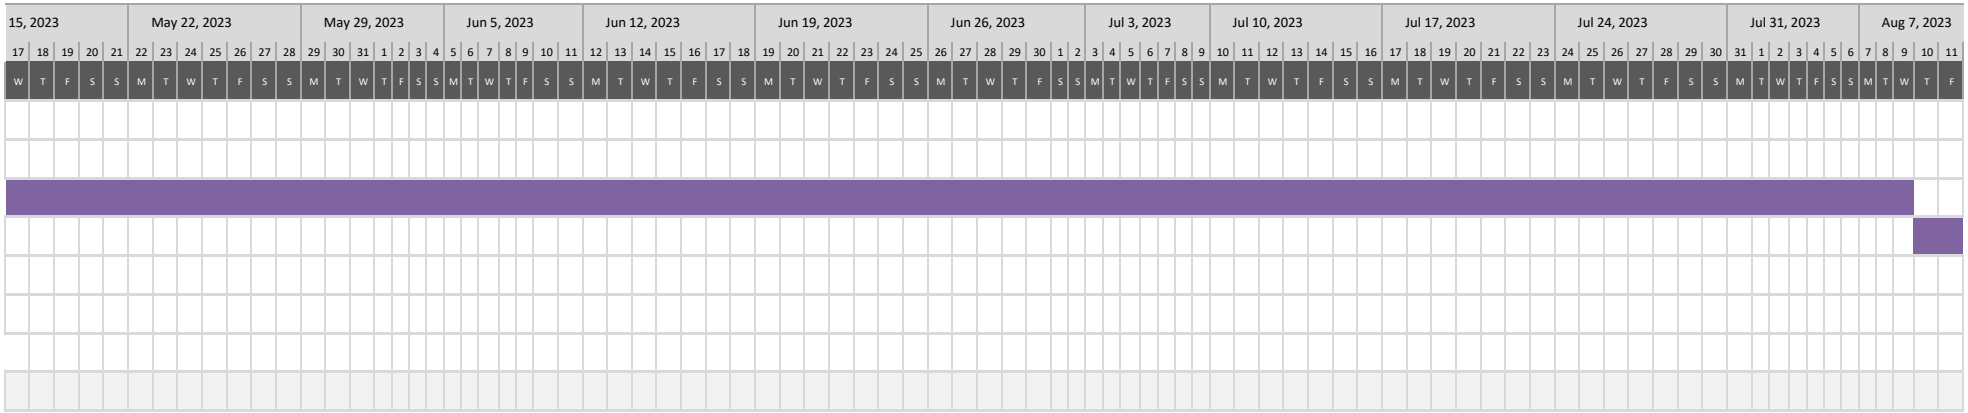
15, 2023
May 22, 2023
May 29, 2023
Jun 5, 2023
Jun 12, 2023
Jun 19, 2023
Jun 26, 2023
Jul 3, 2023
Jul 10, 2023
Jul 17, 2023
Jul 24, 2023
Jul 31, 2023
Aug 7, 2023

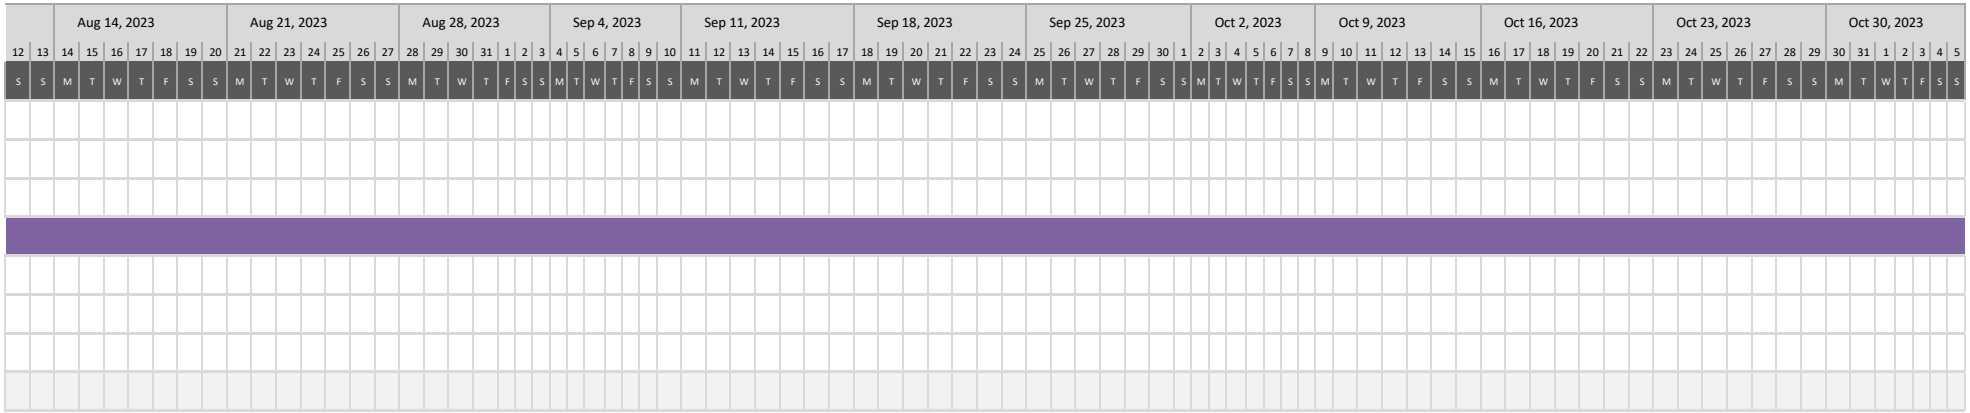
Aug 14, 2023
Aug 21, 2023
Aug 28, 2023
Sep 4, 2023
Sep 11, 2023
Sep 18, 2023
Sep 25, 2023
Oct 2, 2023
Oct 9, 2023
Oct 16, 2023
Oct 23, 2023
Oct 30, 2023
12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5
S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S

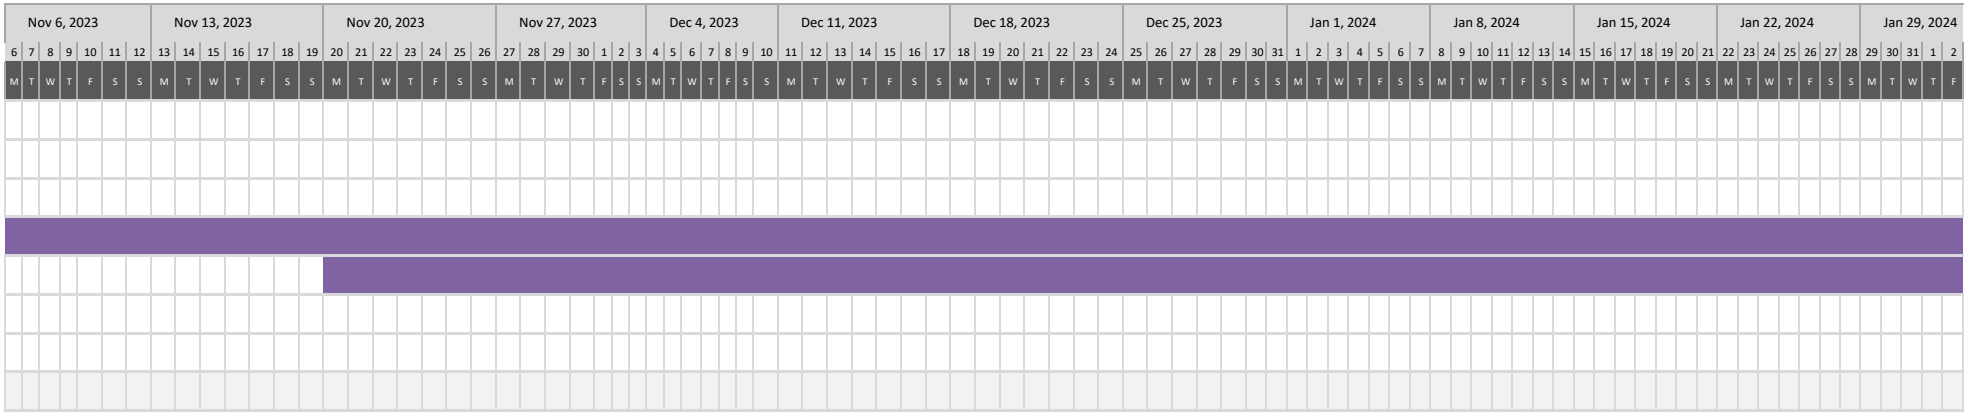
Nov 6, 2023
Nov 13, 2023
Nov 20, 2023
Nov 27, 2023
Dec 4, 2023
Dec 11, 2023
Dec 18, 2023
Dec 25, 2023
Jan 1, 2024
Jan 8, 2024
Jan 15, 2024
Jan 22, 2024
Jan 29, 2024

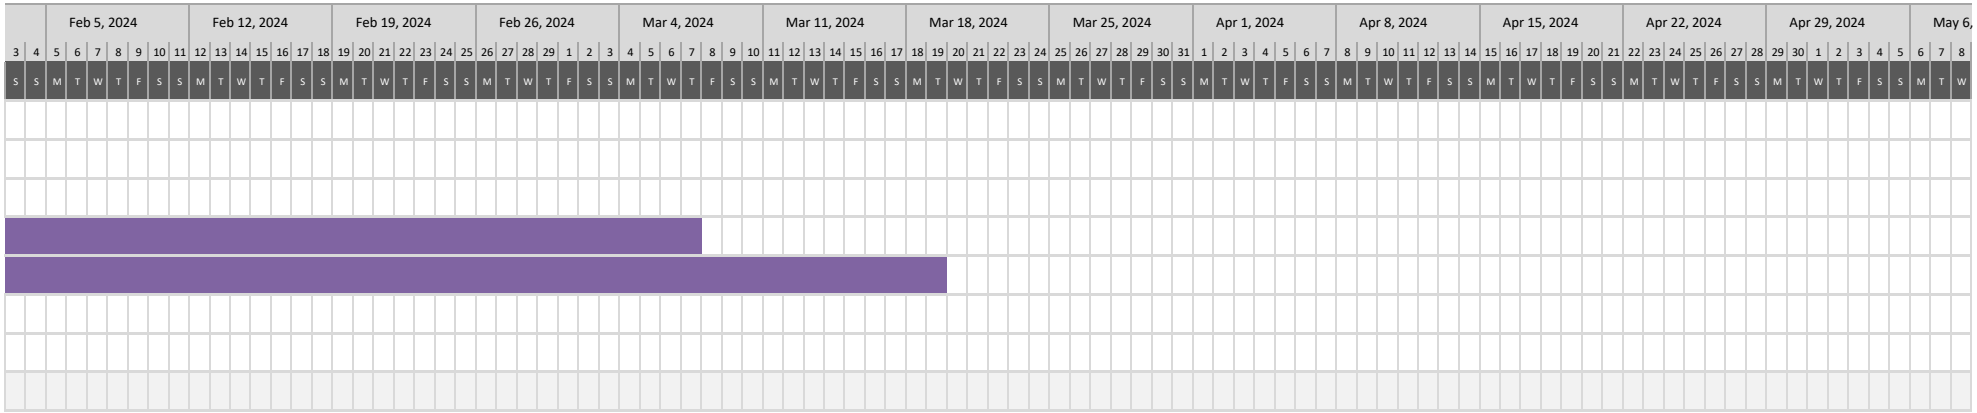
Feb 5, 2024
Feb 12, 2024
Feb 19, 2024
Feb 26, 2024
Mar 4, 2024
Mar 11, 2024
Mar 18, 2024
Mar 25, 2024
Apr 1, 2024
Apr 8, 2024
Apr 15, 2024
Apr 22, 2024
Apr 29, 2024
May 6,

2024				May 13, 2024							May 20, 2024							May 27, 2024						
9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Jun 3, 2024							Jun 10, 2024							Jun 17, 2024							Jun 24, 2024						
3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Jul 1, 2024							Jul 8, 2024							Jul 15, 2024							Jul 22, 2024						
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Jul 29, 2024							Aug 5, 2024							
29	30	31	1	2	3	4	5	6	7	8	9	10	11	12
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Aug 12, 2024						Aug 19, 2024						Aug 26, 2024						Sep 2, 2024						Sep 9, 2024					
13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
